

Villas at Five Ponds Shingles Replacement Project

September 12, 2025

Dear Amy and Board Members,

I hope you're doing well. I wanted to give another quick update on the construction schedule for the Villas at Five Ponds for WEEK # 27. There haven't been any significant changes since our last update: we're still on track to complete all the buildings for both the Red Crew and Blue Crew by the end of this month. After that, we'll continue with the Five Ponds Circle crew until all nine buildings are finished.

Overall, everything is progressing steadily, and at this point, there's nothing notable to report in terms of delays or issues. As we approach the final stages, we will need to gather some information and coordinate one last meeting to wrap up Stage 3. We'll stay on top of all the necessary data and documentation to ensure that goes smoothly.

We're genuinely pleased with how things are moving forward, and we're looking forward to finishing the project strong. We appreciate all the support, and we're confident this will be a great reference project for Lemus Construction moving ahead.


If you have any questions or need additional details, please feel free to reach out.

Best regards,

Mario A. Aguilar
Lemus Construction



OFFICE 214-896-8846
Email: info@lemusconstruction.com

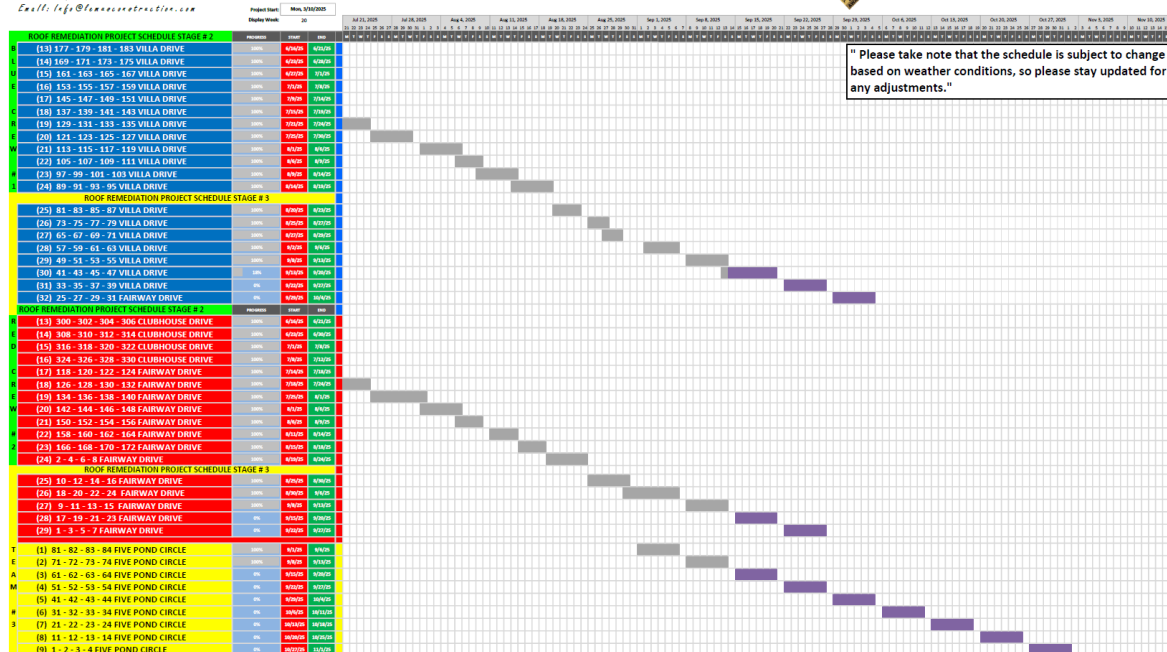

water intrusion. We also noticed that some interior areas, like the bathroom ceiling, have mold and need remediation. This is a step the homeowners will need to take to repair and repaint those areas and fully address the interior damage caused by the previous leaks.

Once they complete that interior work, if there are any further issues, we'll be happy to revisit. However, based on today's inspection, we are confident the roof is sound and watertight.

Please let us know if you need any additional information or have further questions.

Thank you, and we appreciate your cooperation.

Best regards,

Mario A. Aguilar
Lemus Construction

September 5, 2025

Dear Amy and Board Members,

I Hope you're doing well. I wanted to give you a quick update on our progress with the Roofing Project. Please refer to the attached updated Construction Schedule.

We're currently working on the first building at Five Ponds Circle and making solid progress this week, even with the shorter week after the holiday.

Here's the crew-by-crew rundown:

- Red crew: They're working on building 26 and will move to building 27 next week around September 8. They have two more buildings after that and should finish by the end of September.
- Blue crew: They're wrapping up building 28 and then have four more to go, which puts them on track to stay with us until the first week of October.

- Yellow crew: They'll be on-site through most of October to handle all nine of their assigned buildings. We could consider adding another crew (red or blue once they are done with their assigned buildings), but given space constraints, we will keep it as our last resource. It's likely more practical to keep it as is. We are approaching hurricane season, so the weather will determine our decision. We should see them finish around the end of October or early November.


Additionally, I think it's worth mentioning that we've received a lot of positive feedback from crew members and team leads. We're committed to finishing strong. We know it's not just how you start a project but how you finish it, and we'll ensure all open items are addressed before any crew steps out. We'll keep everyone updated as we go.

Feel free to reach out if you have any questions, and thanks again for your support in making this process go smoothly.

Best regards,

Mario A. Aguilar
Lemus Construction

OFFICE 215-994-9944
Email: info@lemusconstruction.com

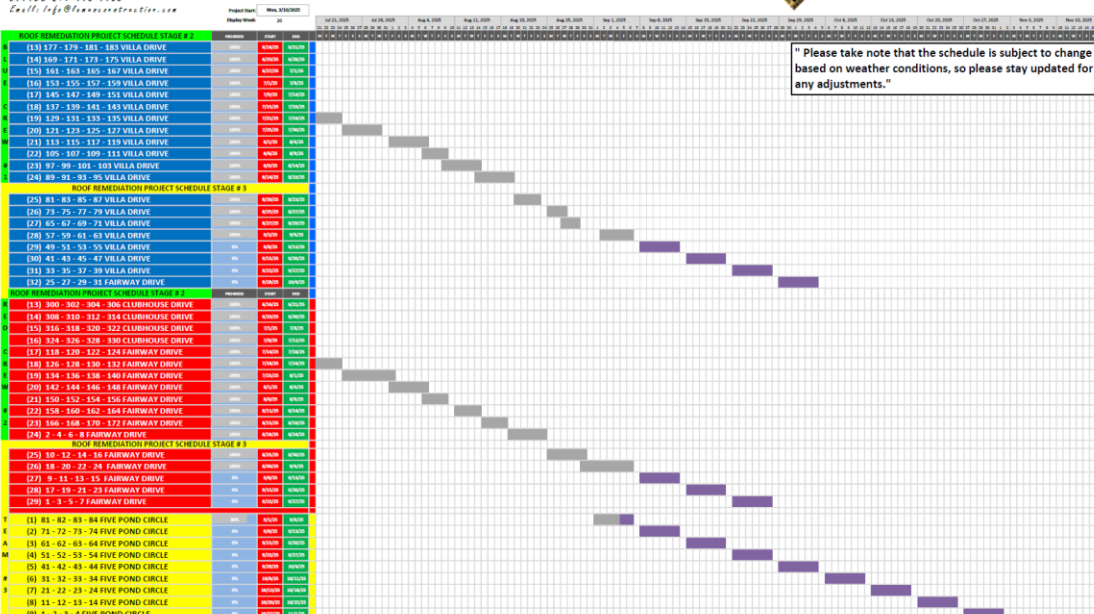

August 28, 2025

Dear Amy and Board Members,

I just wanted to give you all a quick recap of our meeting last Tuesday about Stage 2 of the roofing project. It was a short and productive session with the Board of Directors, and we covered all the open items, especially the billing details. As of now, all individual homeowners have received their bills for Stage 2, and we expect payments to come in over the next two to three weeks. Once that's settled, we'll include Amy so she's up to date on the billing status.

On another note, Stage 2 went more smoothly overall compared to Stage 1, which is great news. As we move into Stage 3, I've attached the updated construction schedule showing the timeline. You'll see that both Wilson and Marco's crews, the original two crews—will finish around the end of September. We're also bringing in a third crew right after Labor Day, and they'll help us wrap up by the end of October. That staggered schedule will give us a smooth transition and extra time to handle any final punch list items.

In preparation for that, today we began dropping material for the third crew at Five Pond Circle ahead of the September 2nd start date. Please see the attached pictures showing the staging area taken for the first building. From there, we will continue clockwise until all nine buildings within the circle are complete.

We expect that as we get closer to finishing, there might be a slight increase in homeowner questions or minor complaints, just because the project has been a long one. Rest assured, we're dedicating time to address those as they come.

Feel free to reach out if you have any questions, and thanks again for your support in making this process go smoothly.

Best regards,

Mario A. Aguilar
Lemus Construction

OFFICE 918-994-9944
Email: info@lemusconstruction.com



August 8, 2025

Dear Amy and Board Members,

I hope this message finds you well.

I want to share a brief update on the latest progress at the Villas at Five Ponds. The past two weeks have brought great momentum. We've gained nearly a full week on our construction schedule, mainly due to better weather conditions. We are now nearing the completion of **Stage 2** of the project, and we are very optimistic about staying on track to finish **by the end of October**.

Please see the attached updated progress schedule reflecting these improvements. Based on our current pace, there is even a possibility of an open week that could let us start Stage 3 slightly earlier than planned. Of course, we will confirm that once we officially close out Stage 2 during our next meeting.

Although not everything has been perfect, we continue to address minor issues and resident concerns as they arise. That said, we've noticed a very positive shift; the community has embraced the project, and many residents have expressed their approval of what they see.

A big thank you to Marco, Wilson, and their teams for their ongoing hard work and dedication. This project is becoming a reality because of their efforts and commitment on the ground every day.

It's meaningful to note that our final meeting will likely take place nearly one year after we were awarded this project. While we're not at the finish line yet, we're not bringing the guard down and staying alert and motivated as we prepare for Stage 3.

Thank you again to the entire Board of Directors and to you, Amy, for your continued support and collaboration. We look forward to successfully completing this project together.

Best regards,

Mario A. Aguilar
Lemus Construction

mobilize them as early as September 3rd instead of the originally projected September 8th. This adjustment could help maintain consistent production and keep us on track for a potential completion of the remaining buildings by the end of October.


Things have been running smoothly overall. That said, if there are any comments, suggestions, or if anything has fallen through the cracks, please don't hesitate to reach out. We're committed to making sure no loose ends are left unaddressed and that the residents feel confident in the process every step of the way.

Thank you again for your collaboration and ongoing support.

Best regards,

Mario A. Aguilar
Lemus Construction

OFFICE 210-996-9966
Email: info@lemusconstruction.com

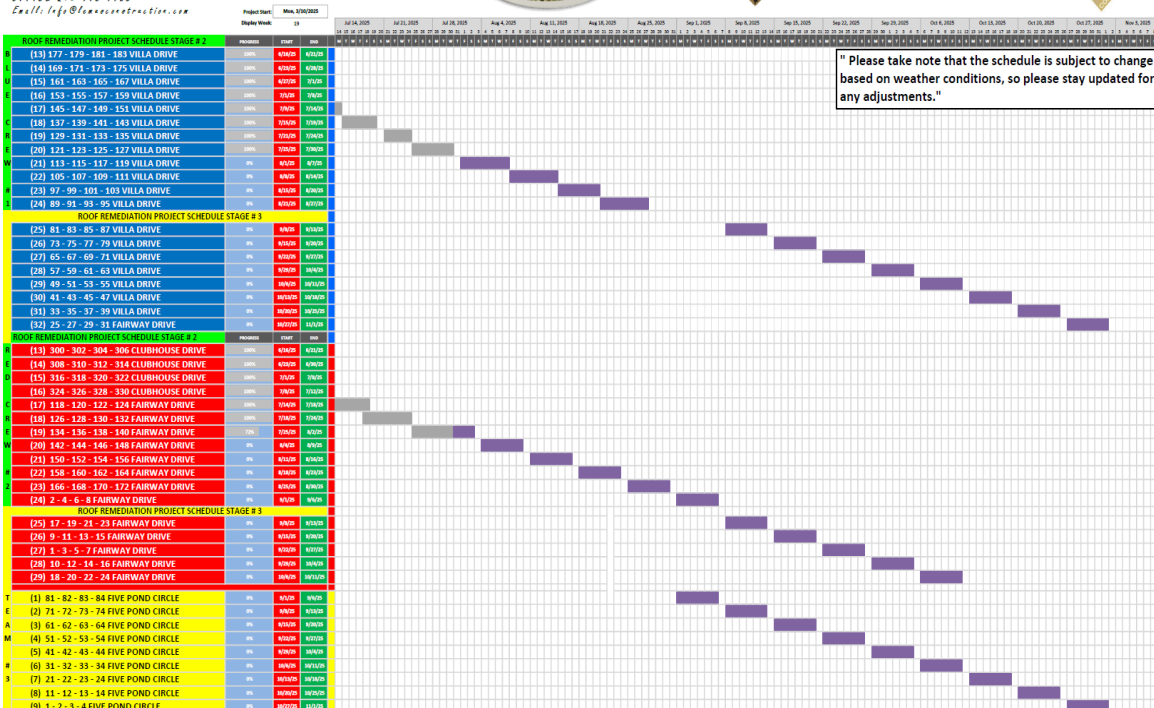

July 10, 2025

Dear Amy and Board Members,

I hope everyone had a relaxing and enjoyable Fourth of July celebration.

As we complete Week 17 of the roof replacement project at The Villas at Five Ponds, I wanted to share our latest construction update. Despite some challenges with recent weather, I'm pleased to report that we remain on track with the *Stage 2* schedule. Attached you will find the most current version of the construction schedule reflecting where we stand today.


Field Activity Update:

1. Red Crew: Completed Building #15 and began work on Building #16 today. Additional roofers have been added to help maintain momentum.
2. Blue Crew: Expected to begin operations on Building #17 tomorrow, July 9th.

One of the board members reached out regarding the large project schedule board inside the clubhouse. We originally planned to revisit and revise the full schedule around mid-July, depending on whether the Board confirms the addition of a third crew to handle the next phase of buildings. While we understand the importance of keeping residents informed, I would advise holding off on printing or displaying a new board version until the week of July 22nd. By then, the Board will hopefully be in a position to formally decide on bringing in the third crew, which has been proposed to begin sometime mid-August or shortly after Labor Day. Posting an interim version now, only to replace it two weeks later, could cause unnecessary confusion among residents.

The project schedule that is posted outside the clubhouse multi-purpose room has been updated with target start and end dates for stage 2 and stage 3.

OFFICE 215-994-9966
Email: info@lemusconstruction.com

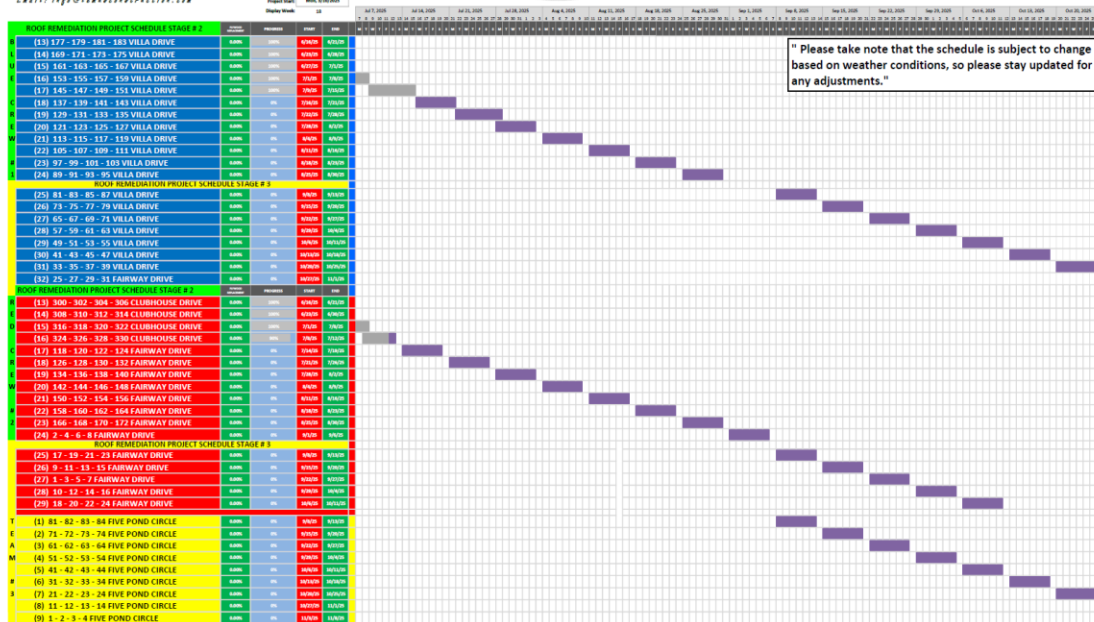

We continue to handle daily homeowner inquiries via phone and email. While some days bring more traffic than others, no open items currently require immediate Board input, aside from the decision about the third crew. We remain empathetic to everyone's concerns and are fully committed to transparency and clear communication. As we prepare for the next stage, rest assured that any adjustments to our operations are made with the goal of ensuring a smooth and successful project delivery.

Please feel free to share any feedback or questions. We're here to support in any way we can.

Warm regards,
Mario A. Aguilar
Lemus Construction

June 27, 2025

Dear Amy and Board of Directors,

Hope you're all doing well.

I just wanted to send a quick update on the status of the roofing project and share the latest revised schedule for the current phase of work.

One of the board members raised a good point about the original building ratings and whether we should still prioritize based on those. To clarify, those ratings were very helpful early on, especially when we planned to complete the project over 3–4 years. Now that we're moving forward full speed and tackling the entire community in a single, large phase, the sequence has been planned based on logistics, staging space, and minimizing daily disruptions for residents. In short, our goal is to keep things smooth, steady, and respectful of everyone's routines while still working efficiently.

That said, if the Board strongly prefers to adjust the building order, we're completely open to that. All we need is a formal request, and we will update the schedule accordingly. Lemus Construction is fully committed to delivering what was promised and to maintaining the strong relationship we've built with the community.

Attached is the revised schedule showing our current progress through Stage Two. Currently, the Blue Crew is slightly ahead of the Red Crew by one building. To help balance the work and stay on track for a late August completion of this stage, we plan to increase the crew size where needed temporarily.


Also, during our last meeting, we mentioned that once we reach Mid-July and have a clearer picture of production, we'll revisit the possibility of adding a third crew to help speed up the overall timeline.

As always, I'm here if you have any questions or want to schedule a quick call to go over anything in more detail. Thanks again for your continued trust in Lemus Construction. We're proud to be part of this project and excited to keep things moving forward.

**Warm regards,
Mario A. Aguilar
*Lemus Construction***



OFFICE 215-786-7866
Sofia@lemusconstruction.com

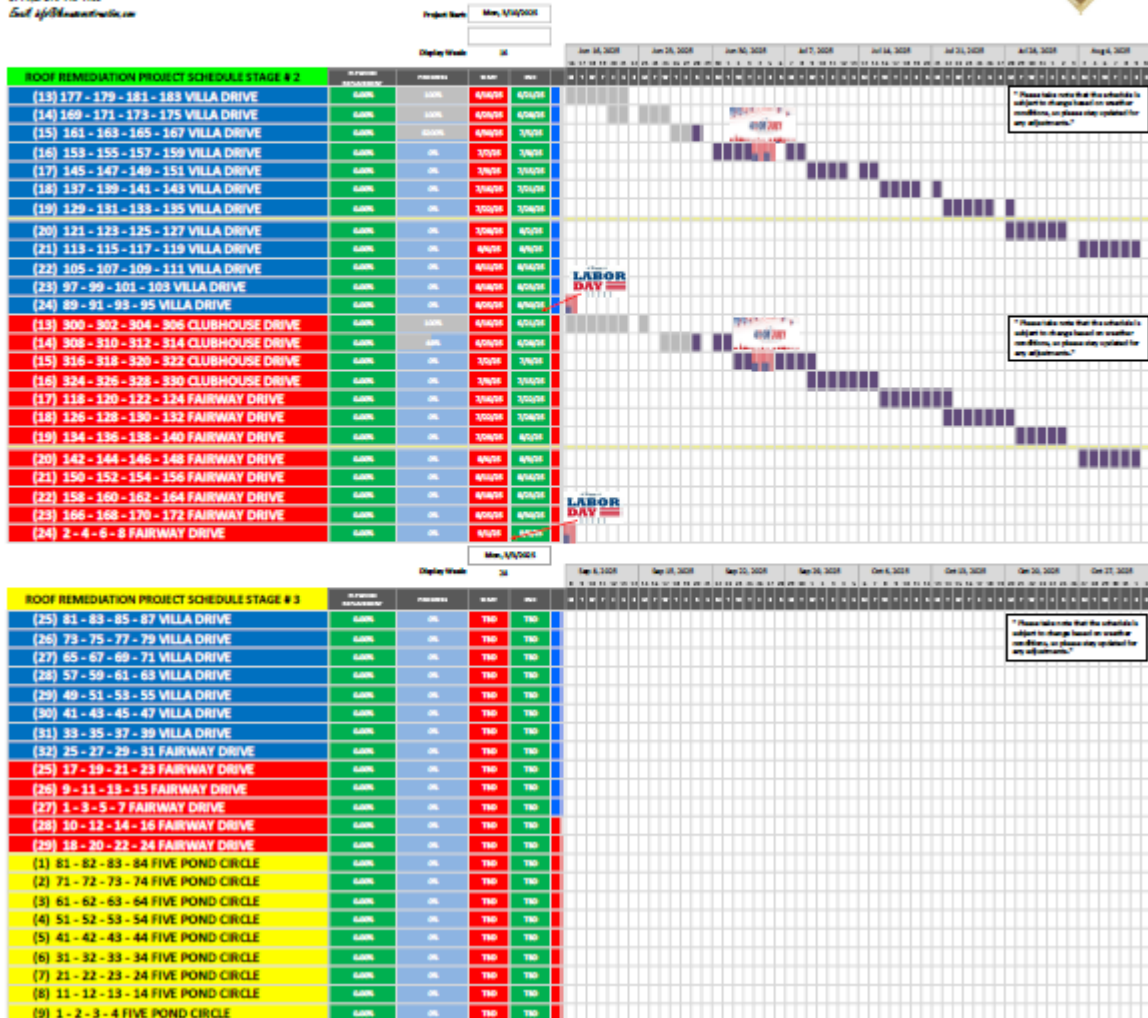

June 16, 2025

Dear Amy,


I hope you are doing well.

As promised, I've reviewed and updated the construction schedule for Stage 2 of the roof remediation project at the Villas at Five Ponds. Please find the revised PDF file attached for your reference.

Between now and mid-July, we will closely monitor progress and conditions to determine whether adding a third crew is necessary. This would ensure that the entire project is completed by mid-October or early November at the latest, even considering potential weather delays or unforeseen circumstances.

I will follow up with another email later this week based on the current week's production, so we can keep everything aligned and on track.

Warm regards,
Mario A. Aguilar
Lemus Construction

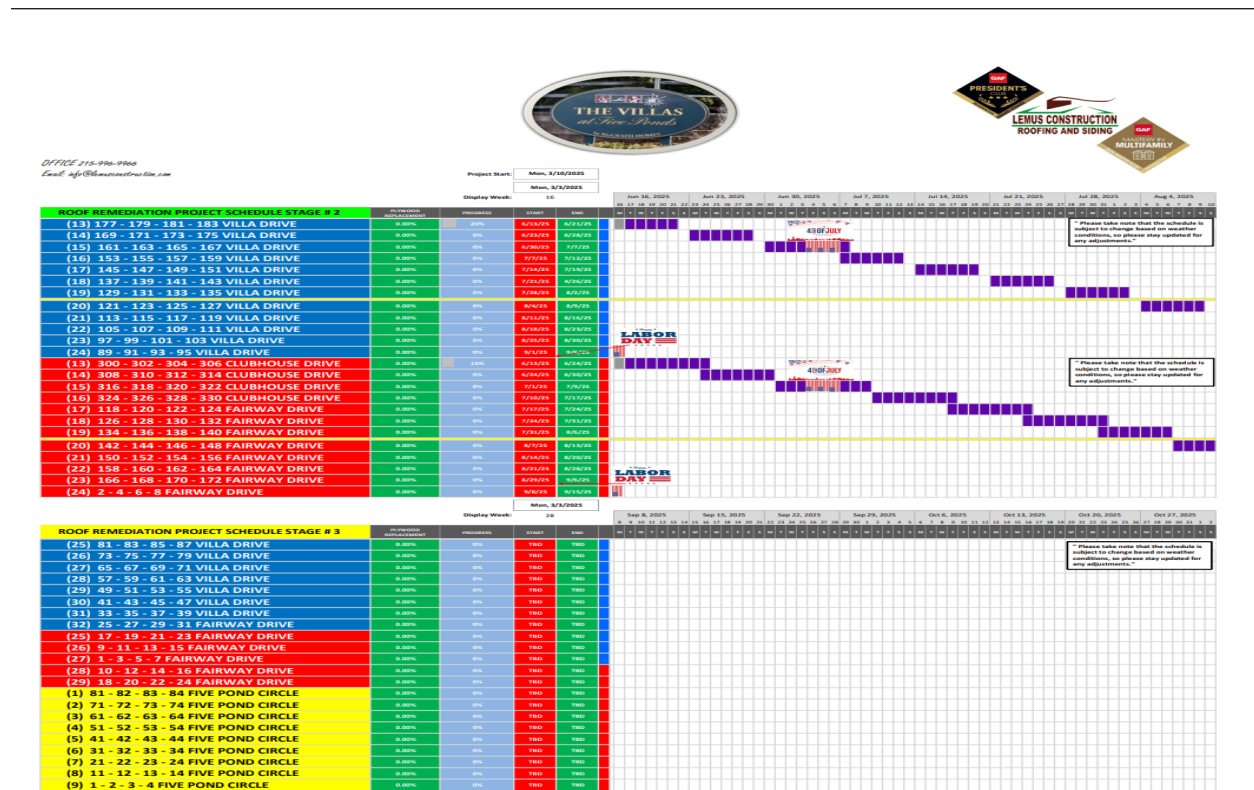

June 6, 2025

Dear Amy,

I hope you're doing well. We are grateful for the good weather this week! Following up on my previous message, I'd like to confirm that we are approaching the successful completion of Stage 1 at the Villas at Five Ponds. We remain on track to complete all 24 buildings by Monday, June 9th, and I have designated Tuesday, June 10th as the day for our teams to conduct a full walkthrough of the completed buildings. As we near this important project milestone, I'd also like to take the opportunity to outline the next steps planned for the week ahead.

1. Final Walkthrough – Stage #1 Buildings (Tuesday, June 10th)

We have tentatively scheduled Tuesday, June 10th for a full-day walkthrough of all 24 buildings completed during Stage #1. This will mark our third round of inspections. Our roofing teams will revisit each roof section to verify that all details have been addressed. At the same time, the siding crews will finalize any remaining trim, siding, or gutter work, and our full team will perform a thorough cleanup of the surrounding areas.

We kindly request that a memo be circulated to the residents of the Stage #1 buildings to inform them of our presence. While minimal disturbance is expected, please note that our crews will be on the roofs and around the building exteriors throughout the day.

2. Launching Stage #2 (Post-Walkthrough)

Following the walkthrough, and pending confirmation, we plan to begin Stage #2 with the following buildings:

- Blue Crew: 177, 179, 181, 183 Villa Drive (Building #13 on the schedule)
- Red Crew: 300, 302, 304, 306 Clubhouse Drive (Building #13 on the schedule)

This staging will ensure a seamless transition into the next phase and allow both crews to maintain strong momentum.

We're proud of the progress we've achieved together and remain fully committed to delivering a successful outcome. If there are any questions or additional coordination items to review before next week, please don't hesitate to reach out.

**Warm regards,
Mario A. Aguilar
Lemus Construction**

May 30, 2025

Dear Amy,

I hope this message finds you well.

We are now finishing week #12 of production for the Villas at Five Pond roof remediation project, or week #13 if we include the Clubhouse roof replacement. Although our original goal was to complete the first stage by this point, the weather had other plans. Nonetheless, we remain optimistic and committed to our objective of completing all buildings before the end of the year, which aligns with the expectations set during our earlier meetings, particularly the focus on addressing the older roofs and

those with active issues prior to next winter. I've attached the Updated Construction Schedule below.

We are approaching the final stretch of Stage 1 and are confident that we will complete the first 24 buildings by June 14th.

Warm regards,
Mario A. Aguilar
Lemus Construction

May 16, 2025

Dear Amy,

I hope this message finds you well.

As expected, this week's production was significantly impacted by unfavorable weather conditions. Despite the delays, we are continuing to follow the original plan to complete the first phase of 24 buildings (one-third of the community) before requesting a meeting with the Board for a project review and next steps.

We are also actively evaluating contingency plans in case we fall behind schedule, with the goal of ensuring that all 72 buildings are completed within the 2025 season.

In the meantime, we would like to inform you that, weather permitting, our crews are planning to work tomorrow, Saturday, May 17, to regain some lost time.

Please don't hesitate to reach out if there are any concerns. We appreciate your continued support and communication throughout the project.

Best regards,
Mario Aguilar
Lemus Construction

May 7, 2025

Dear Amy,
I hope you're doing well.

There isn't much to report from last week in terms of production; it was steady and pretty smooth, as expected. Given the current weather forecast and the recent and ongoing rain, this week will be largely unproductive, a situation we anticipated.

After a brief absence from the site the last two days, we received a few calls from residents looking for updates. Fortunately, there was nothing urgent or concerning that requires further discussion. That said, we'll be making some operational adjustments to

improve our day-to-day transitions between completed buildings and those scheduled next. Our goal remains to keep the project moving as smoothly and efficiently as possible, even with weather-related setbacks. We will also implement a plan to prevent debris from our work from entering the underground piping; some of these have collected organic debris and shingle granules over the years and appear to be clogged. We can discuss this at our Completion Meeting for stage #1.

Later this week, I will also be sending an updated construction schedule to help assess where we stand in completing the first stage and to allow a couple of days to revisit the 24 completed roofs before launching the next phase of the project.

With that in mind, would it be possible to get authorization to work this coming Saturday? This would allow us to make up for at least part of the three days lost to rain and help us stay closer to the projected timeline.

Please let me know if the Board is open to this request and thank you again for your continued support.

**Best regards,
Mario Aguilar
Lemus Construction**

April 25, 2025

As we complete week #8 of operations at the Five Pond Villas Community, we are pleased to report that the project is progressing smoothly and on schedule.

Although we initially lost some time due to adverse weather conditions, we successfully recovered several of those days by utilizing an additional labor force. As of today, the schedule indicates that the crews are on track to complete the first stage of 12 buildings by the first week of June. Minor complaints and concerns from residents have been addressed promptly along the way, which has helped maintain a positive flow of operations and communication.

We are now preparing to send the second batch of invoices, covering another 6 buildings. Based on recent feedback, we believe that the adjustments made to our documentation and communication processes with residents will have a much greater positive impact compared to the first billing cycle.

Regarding the concern about the attic fan at the pool house: Following our meeting with Mark, our team returned later that afternoon to double-check the unit, and we confirmed that the fan is indeed functioning properly. This power fan is equipped with a thermostat and humidistat.

Looking ahead, as temperatures begin to rise, we do anticipate that production may slow slightly due to weather conditions. However, at this point, there are no major issues to report, and we remain committed to maintaining the project's momentum.

Thank you for your continued support and partnership.

Please feel free to reach out if you have any questions or need additional information.

Best regards,

Mario A. Aguilar
Lemus Construction

April 10, 2025

Dear Amy,

I hope this message finds you well.

As we conclude Week #6 of the roof remediation project, I wanted to provide you with an updated construction schedule and highlight some important observations from the past few weeks. As expected during spring, the weather conditions throughout April have posed significant challenges, resulting in about one full week of lost production due to rain and high winds. Despite these setbacks, we are committed to making up for the delays and adjusting our workflow to stay as close to the schedule as possible.

Our crews are continuing to progress, and we are currently finishing work on the last building from our most recent email (4 for both crews) that required additional time on-site due to weather interruptions. We appreciate everyone's patience and flexibility as we navigate these seasonal challenges.

The first round of billing was sent out last week. While we initially anticipated a more resistant response, we have noticed that residents are gradually beginning to accept the additional charges associated with unit-specific plywood and attic work. For those who have requested it, we are providing photo documentation to clarify the necessity of these repairs. However, we've observed that close-up images can sometimes create doubt, as homeowners occasionally question whether the documentation corresponds to their unit. On the other hand, wider photos may not clearly show the level of plywood deterioration. Our Project Managers have been instructed to maintain detailed records moving forward, including time-stamped and unit-specific images to support all documented work.

The memo you kindly helped distribute seems to have been effective in providing additional context, and we hope it continues to assist in managing expectations in the coming weeks.

We understand that we are still in the early stages of this large-scale project, and we remain focused on quality execution and transparent communication. Please find attached the updated construction schedule that reflects our current position and adjusted timeline.

Additionally, as we prepare for next week's workflow, we kindly ask for your confirmation on whether we are permitted to work on Good Friday. This will help us better coordinate labor and logistics as we aim to recover lost time.

Lastly, we want to express our sincere gratitude for the ongoing support from both management and the Board of Directors. Your trust and collaboration have been invaluable as we navigate the challenges of this season and remain focused on delivering a successful outcome for the community.

As always, please feel free to reach out with any questions, and we will be happy to assist.

Best regards,

Mario A. Aguilar
Lemus Construction

April 3, 2025

Dear Amy,

I hope you're doing well. Unfortunately, the weather hasn't been in our favor this week, but overall, things are going smoothly. We're confident that we'll be able to make up for the lost days and stay on track.

Invoices for the first six buildings were sent out earlier this week, and as you may be aware, we would appreciate your support in sharing the attached memo. This is in anticipation of potentially receiving additional concerns or complaints, similar to those from Unit XXX, where our explanations regarding homeowner responsibility for extra work were not well received. We kindly request your assistance in distributing the attached memo to all unit owners.

This memo is intended to provide clear, transparent communication regarding the scope of additional work discovered during the roofing project - specifically items such as damaged plywood, bathroom vent corrections, attic fan removals, and other repairs that fall under individual homeowner responsibility. As discussed during our open meeting at the clubhouse and outlined in the prior communications, these items are essential to ensure the long-term integrity of the new roof system and to maintain compliance with the Golden Pledge Warranty standards.

We believe that by sharing this information proactively, we can help minimize confusion and provide clarity on why these costs are necessary, as well as the care we take to do the right thing for each homeowner's property.

Please see below for Lemus communication regarding the scope of additional work discovered during the assessment of each homeowner's roof. As always, thank you for your continued support and collaboration.

Best regards,
Mario A. Aguilar



ROOFING | SIDING | DECKS

Specializing in Multi-Family and Commercial Exterior Renovations!

Apr 3, 2025



Memo: Project Clarification – Villas at Five Ponds Roof Replacement

Dear Residents,

We hope this message finds you well. As the roof remediation project continues across the Villas at Five Ponds community, we want to take a moment to clarify a few important details and address some of the recent concerns we've received from homeowners. First and foremost, we appreciate the opportunity to work in your community and understand that projects of this magnitude can be disruptive. Our goal remains to deliver a high-quality roof system backed by the GAF Golden Pledge Warranty — a top-tier protection that reflects our commitment to durability, workmanship, and peace of mind.

Scope of Work – Homeowner Responsibility

During our open meeting in **November, 2024** and in follow-up communication distributed by management, we outlined that certain items discovered inside the attic space fall under individual homeowner responsibility. These include:

- Replacement of deteriorated or damaged plywood sheathing.
- Bathroom fan duct connections.
- Attic fan removal.

These were not arbitrary decisions. Rather, these repairs are necessary to maintain the structural and functional integrity of your new roof system.

📞 215-996-9966 (PA) | 908-237-3655 (NJ)

🏠 680 Sycamore Dr, Warminster, PA 18974
(Headquarters)
79 US Hwy 202, #301, Ringoes, NJ 08551

🌐 www.lemusconstruction.com

✉ info@lemusconstruction.com

Follow Us





ROOFING | SIDING | DECKS

Specializing in Multi-Family and Commercial Exterior Renovations!

We ask:

“What would you think of a contractor who knowingly left behind compromised roof decking beneath a brand-new roof?”

That's not how we operate. We chose to replace those sections immediately, preserving your investment and maintaining compliance with the Golden Pledge Warranty. This work falls under homeowner responsibility as it is specific to individual unit conditions.

It's important to emphasize that we do not profit from plywood replacement. In fact, this type of work often slows down the production process. However, we treat each home as if it were our own. If we discover compromised sheathing during removal and choose to leave it behind, not only would that reflect poor workmanship, but it would also jeopardize the long-term performance of the new shingles. Our decision to replace this material is rooted in doing what is right — not what is easiest.

- **Bathroom Vent Ducting**

In the first buildings completed, we discovered that many bathroom fans had flexible ducts left disconnected or terminated improperly inside the attic, allowing moist air to circulate and contributing to condensation and mold risk. We took the initiative to correct this issue during roofing, utilizing existing materials where possible to minimize added costs, and only billing for the time needed to make these vital corrections.

Please keep in mind that the timeframe to complete these repairs is limited, as we must fully close and seal each area by the end of the day to protect your unit from weather exposure.

- **Attic Fan Removal**

As part of the new roofing system, any existing power attic fans must be removed in order to comply with GAF's shingle manufacturer installation standards. These systems are being phased out in favor of balanced passive ventilation (ridge vents and intake vents) which improves energy efficiency and eliminates conflict between different exhaust sources. Removal of attic fans carries an additional cost, which has been clearly itemized in homeowner invoices.

📞 215-996-9966 (PA) | 908-237-3655 (NJ)

🏠 680 Sycamore Dr, Warminster, PA 18974
(Headquarters)
79 US Hwy 202, #301, Ringoes, NJ 08551

🌐 www.lemusconstruction.com

✉ info@lemusconstruction.com

Follow Us     



ROOFING | SIDING | DECKS

Specializing in Multi-Family and Commercial Exterior Renovations!

Important Note on Warranty Eligibility

Please be advised that the **GAF Golden Pledge Warranty** is a collective certification that applies to the entire building as a unit. This means that if any resident within a quad fails to remit payment for their portion of the additional work, we will be unable to process and submit the warranty registration for that building. Unfortunately, **GAF will not honor or issue partial warranties on shared structures.**

We strongly encourage each homeowner to fulfill their responsibility so the building as a whole may benefit from the full 25-year labor and materials coverage that this premium warranty provides.

We remain committed to quality, transparency, and doing what's best for both the homeowners and the HOA. Should you have any further questions or require clarification, please don't hesitate to reach out to our team.

Sincerely,
Lemus Construction, Inc.

☎ 215-996-9966 (PA) | 908-237-3655 (NJ)

🏠 680 Sycamore Dr, Warminster, PA 18974
(Headquarters)
79 US Hwy 202, #301, Ringoes, NJ 08551

🌐 www.lemusconstruction.com

✉ info@lemusconstruction.com

Follow Us     

March 28, 2025

Dear Amy,

I hope this email finds you well. As we complete Week 4 of the roof replacement project, I'm pleased to report that everything is moving right along with the anticipated project schedule. The crews have built strong momentum, and our process continues to improve with each completed building.

While progress remains steady, we do anticipate losing a couple of days next week due to the weather forecast. We'll continue to monitor the conditions closely and make necessary adjustments to the schedule to stay on track as much as possible.

Throughout the week, our team addressed minor items such as vent terminations and flashing adjustments. We've also received a few resident comments and minor concerns, all of which have been promptly handled as part of our ongoing daily operations. At this time, there are no major issues to report. We continue to log all unit-specific additional work, which will be itemized and reflected in the upcoming billing cycle.

We're grateful for the ongoing support and patience from the residents — by now, we've even started making a few friends along the way! Our team remains committed to delivering what was promised during the open meeting: a top-quality roofing system, installed with precision and extra care.

We've noticed that some drivers become distracted while observing the roofing work in progress and are unaware of nearby equipment or dumpsters. As a proactive safety measure, we will be placing temporary speed bumps in areas where dumpsters are located. I'm currently waiting for "Speed Bump Ahead" lawn signs, and once they arrive, the bumps will be installed to help manage traffic more safely during active construction. We are approaching completion of the first group of six buildings and will begin processing homeowner billing for their portion of the completed work.

Please let us know if there are any questions, suggestions, or additional support we can provide. We appreciate your partnership and look forward to continuing the project with the same momentum and care.

Best regards,

Mario A. Aguilar

Lemus Construction

March 21, 2025

Any updates we receive from Lemus Construction about the Villas at Five Ponds "shingle replacement project" seem to come late Friday or Monday, upon receipt we will post it on our website.

So please keep checking it.

In addition, the Shingles Replacement project plan with targeted dates for Phase 1 has been posted outside the multipurpose room. A few copies of the project plan are located on the reception desk. It is also posted on the website. Please note the target dates are the goals of the project. Circumstances beyond the control of the project such as inclement weather or a quad that has issues that will preclude the ability to complete their roof replacement within the week will delay the subsequent shingles replacement on the quads that follow. Thank you for your patience and understanding.



Good afternoon, Amy,

As we conclude Week 3 of the roofing remediation project at Villas at Five Ponds, I am pleased to share that we are making steady and efficient progress. We are refining our workflow and addressing any unexpected challenges that arise.

Having completed work on the first four buildings, we now have a better understanding of the layouts and how unforeseen additional work can impact our production. With this knowledge, we have adjusted our approach and are currently nearing completion of the second set of buildings. Although we have encountered a few minor issues, we are addressing these promptly as we move into the next set of buildings. Things are looking up, and I believe we can only improve from here!

General Notes:

1. This week, both the Red Crew and the Blue Crew made significant progress on the second set of buildings. They gained a better understanding of the layouts and production efficiency.
2. We are nearing completion of this week's task, with only minor detail work left to finalize before moving on. Despite a challenging start to the project, we are now heading in the right direction and streamlining our approach to ensure quality and efficiency.
3. Due to strong winds, we will evaluate the safety of removing the remaining portion of the roof at 102-108 Villa Drive today. If conditions are not favorable, we will return tomorrow to complete the task. The next set of buildings is still on schedule for next week, and notices have already been delivered to residents.
4. As we improve our workflow, each adjustment enhances our efficiency and execution. We sincerely appreciate the residents' patience and cooperation, which have helped us maintain smooth operations despite initial challenges. By now, Marco and Wilson have made new friends, and we feel very optimistic about the future!
5. As noted in prior updates, we will begin processing homeowner billing once the next set of buildings is completed.

We appreciate everyone's continued support and collaboration as we move forward in this large-scale project. We will keep you informed of any major developments and continue to provide weekly progress reports.

Please let us know if you have any questions. Looking forward to another productive week ahead!

**Best regards,
Mario A. Aguilar
Lemus Construction**

March 17, 2025

Amy is working on a process to get a written weekly update from Lemus Construction on our now on-going Community "shingle replacement project". Once this process is in place, the updates will be placed on our community website.

Here is the first "home" shingle replacement update:

As we conclude Week 2 of the roofing remediation project at Villas at Five Ponds, I am pleased to report that we are making steady progress as we navigate through the initial phase of the work.

General Notes:

- This week marked the official start of the project, focusing on the designated buildings for Stage #1. Both Crews <Red> and <Blue> started their first building.
- We successfully completed the roof replacement for Units 273-279 Fairway Drive <Blue Crew>
- The roof replacement for Building 110-116 Villa Drive, Red Crew, is nearly complete, with just one more day of work remaining.

- We faced some challenges at the start of the project, encountering active leaks in several areas, particularly around the dormers over the garage roofs.
- Despite these initial setbacks, we gained momentum and completed two buildings this week while identifying areas for efficiency improvements moving forward.
- To help alleviate traffic issues, we placed no-parking signs around Fairway Drive, specifically in areas surrounding the dumpster located in the street. This, together with the email blast sent by management, has been effective in reducing congestion.
- We will keep the option of installing a speed bump available should we find it necessary to implement additional measures.
- While we have completed the roof replacements, there are still detail-oriented tasks remaining on both buildings, including:
 - Siding reinstallation
 - General clean-up
- As the project progresses, we anticipate that the workflow will become more streamlined, allowing for an even smoother process.
- We are closely tracking additional work performed on each individual unit to ensure accurate billing. We plan to submit the first set of invoices once we have completed work on six buildings.
- According to the current forecast, we anticipate rain on Monday. However, if conditions clear up, we will proceed as scheduled while monitoring the situation closely.
- Start notices will be delivered tomorrow morning to keep residents informed. Each crew will be working on Building #2, respectively.

We will keep you updated on any significant changes and provide weekly progress reports on the overall project. This is to ensure transparency and alignment throughout the process. We appreciate everyone's continued support and cooperation as we navigate these critical phases. Please feel free to reach out with any questions or concerns. We look forward to another productive week ahead!

***Best regards,
Mario A. Aguilar
Lemus Construction***

Good afternoon, Amy,

Thank you for reaching out and sharing your observations about the roof replacement project. We appreciate your attention to detail and your patience as we work through this process. I apologize for the delay in responding to your email; I wanted to give the crews time to complete the first two buildings and review the final results of the siding reinstallation.

As part of the roof replacement, certain areas of siding will need to be temporarily removed to properly install new step flashing and ensure a watertight seal. This is an industry best practice that helps protect the long-term integrity of the new roof system and prevents future leaks. Additionally, the installation of ice and water shield is a mandatory

requirement for the GAF Golden Pledge Warranty standards. We discussed this process during the Homeowner Open Meeting on November 14, 2024.

It is important to note that during this process, some incidental damage to the existing Tyvek or siding may occur. This is why we included a carpentry/repair line item in the project scope. While this provision primarily covers pre-existing deteriorated siding, Lemus Construction will also replace any siding or J-channel that sustains damage during the removal process at no cost to the homeowner.

To clarify, homeowners are not responsible for replacing siding that was in good condition prior to the removal. However, they may be responsible for replacing pre-existing deteriorated siding identified during the work. Our team takes great care in re-installing the siding properly, and any damage directly caused by the removal process will be addressed as part of the agreed scope.

All replaced materials will be installed according to manufacturer specifications and best practices, ensuring their functionality and durability. Furthermore, the new roofs are covered under the GAF Golden Pledge Warranty, which provides 100% coverage on labor and materials for the first 25 years.

We appreciate your patience and cooperation as we continue with the project. If you have any further questions, please feel free to reach out, and we will ensure that the Board is kept updated.

Best regards,
Mario A. Aguilar

March 11, 2025

Resident Notifications and Project Kickoff

- We have distributed start notice letters via door hangers to residents in the first two buildings scheduled for work next week.
- As we begin, we appreciate everyone's collaboration as we work through each structure, identify existing deficiencies, and determine the best remediation approach.
- Once the first two buildings are completed, we will compile a detailed progress report, including any findings that may impact the broader project scope, and provide an updated construction schedule.

We have also captured drone footage of the newly installed roof at the clubhouse. This footage will serve as both a record of progress and a visual representation of the improvements being made.

We appreciate the cooperation and support of all involved and look forward to the smooth continuation of the project. Please let us know if there are any additional concerns or if further coordination is needed.

**Best regards,
Lemus Construction**

March 9, 2025

Effective Sunday, March 9th, the Villas at Five Ponds Clubhouse is open as the roof replacement has been completed.

MARCH 1, 2025

The Villas at Five Ponds Clubhouse will be closed from Monday, March 3rd through Saturday March 8th while the Clubhouse Roof is being replaced.
