OFFICE 215-996-9966
Email: info@lemusconstruction.com

Project Start: Mon, 3/10/2025
Display Week: 19

" Please take note that the schedule is subject to change based on weather conditions, so please stay updated for any adjustments."
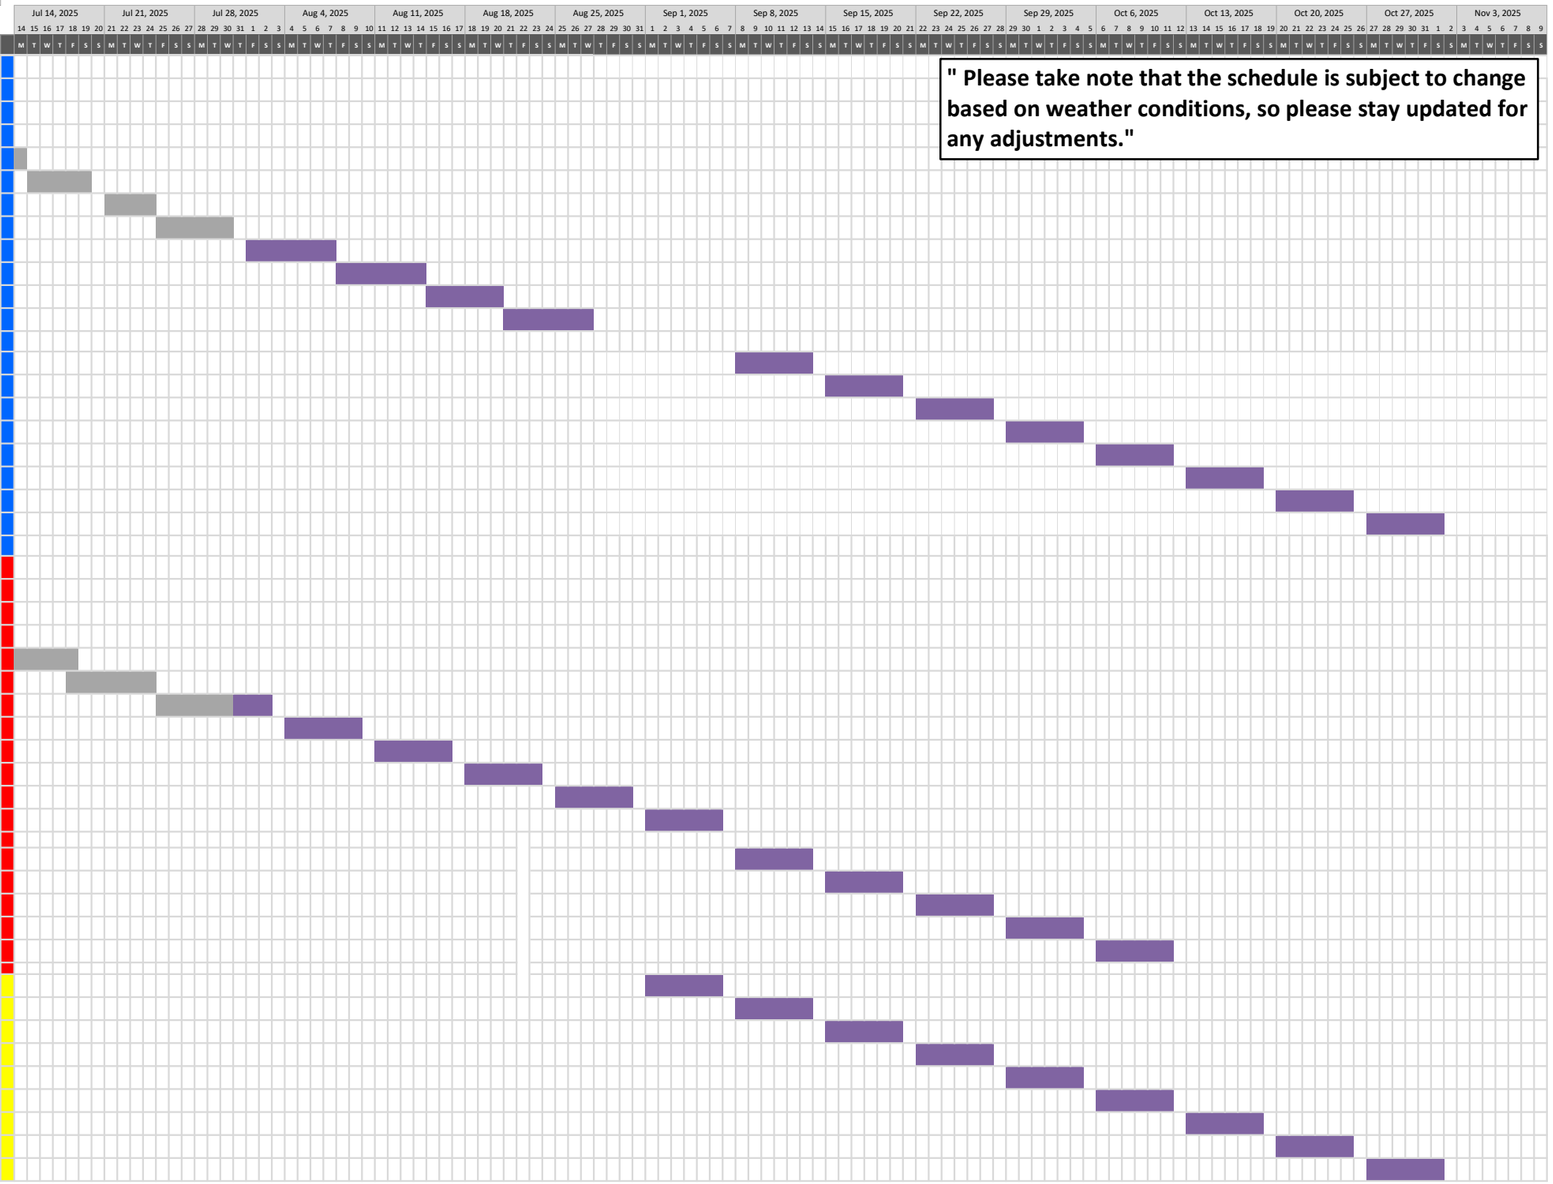
	ROOF REMEDIATION PROJECT SCHEDULE STAGE # 2	PROGRESS	START	END
B	(13) 177 - 179 - 181 - 183 VILLA DRIVE	100%	6/16/25	6/21/25
L	(14) 169 - 171 - 173 - 175 VILLA DRIVE	100%	6/23/25	6/28/25
U	(15) 161 - 163 - 165 - 167 VILLA DRIVE	100%	6/27/25	7/1/25
E	(16) 153 - 155 - 157 - 159 VILLA DRIVE	100%	7/1/25	7/8/25
	(17) 145 - 147 - 149 - 151 VILLA DRIVE	100%	7/9/25	7/14/25
C	(18) 137 - 139 - 141 - 143 VILLA DRIVE	100%	7/15/25	7/19/25
R	(19) 129 - 131 - 133 - 135 VILLA DRIVE	100%	7/21/25	7/24/25
E	(20) 121 - 123 - 125 - 127 VILLA DRIVE	100%	7/25/25	7/30/25
W	(21) 113 - 115 - 117 - 119 VILLA DRIVE	0%	8/1/25	8/7/25
	(22) 105 - 107 - 109 - 111 VILLA DRIVE	0%	8/8/25	8/14/25
#	(23) 97 - 99 - 101 - 103 VILLA DRIVE	0%	8/15/25	8/20/25
1	(24) 89 - 91 - 93 - 95 VILLA DRIVE	0%	8/21/25	8/27/25
	ROOF REMEDIATION PROJECT SCHEDULE STAGE # 3			
	(25) 81 - 83 - 85 - 87 VILLA DRIVE	0%	9/8/25	9/13/25
	(26) 73 - 75 - 77 - 79 VILLA DRIVE	0%	9/15/25	9/20/25
	(27) 65 - 67 - 69 - 71 VILLA DRIVE	0%	9/22/25	9/27/25
	(28) 57 - 59 - 61 - 63 VILLA DRIVE	0%	9/29/25	10/4/25
	(29) 49 - 51 - 53 - 55 VILLA DRIVE	0%	10/6/25	10/11/25
	(30) 41 - 43 - 45 - 47 VILLA DRIVE	0%	10/13/25	10/18/25
	(31) 33 - 35 - 37 - 39 VILLA DRIVE	0%	10/20/25	10/25/25
	(32) 25 - 27 - 29 - 31 FAIRWAY DRIVE	0%	10/27/25	11/1/25
	ROOF REMEDIATION PROJECT SCHEDULE STAGE # 2	PROGRESS	START	END
R	(13) 300 - 302 - 304 - 306 CLUBHOUSE DRIVE	100%	6/16/25	6/21/25
E	(14) 308 - 310 - 312 - 314 CLUBHOUSE DRIVE	100%	6/23/25	6/30/25
D	(15) 316 - 318 - 320 - 322 CLUBHOUSE DRIVE	100%	7/1/25	7/8/25
	(16) 324 - 326 - 328 - 330 CLUBHOUSE DRIVE	100%	7/8/25	7/12/25
C	(17) 118 - 120 - 122 - 124 FAIRWAY DRIVE	100%	7/14/25	7/18/25
R	(18) 126 - 128 - 130 - 132 FAIRWAY DRIVE	100%	7/18/25	7/24/25
E	(19) 134 - 136 - 138 - 140 FAIRWAY DRIVE	72%	7/25/25	8/2/25
W	(20) 142 - 144 - 146 - 148 FAIRWAY DRIVE	0%	8/4/25	8/9/25
	(21) 150 - 152 - 154 - 156 FAIRWAY DRIVE	0%	8/11/25	8/16/25
#	(22) 158 - 160 - 162 - 164 FAIRWAY DRIVE	0%	8/18/25	8/23/25
2	(23) 166 - 168 - 170 - 172 FAIRWAY DRIVE	0%	8/25/25	8/30/25
	(24) 2 - 4 - 6 - 8 FAIRWAY DRIVE	0%	9/1/25	9/6/25
	ROOF REMEDIATION PROJECT SCHEDULE STAGE # 3			
	(25) 17 - 19 - 21 - 23 FAIRWAY DRIVE	0%	9/8/25	9/13/25
	(26) 9 - 11 - 13 - 15 FAIRWAY DRIVE	0%	9/15/25	9/20/25
	(27) 1 - 3 - 5 - 7 FAIRWAY DRIVE	0%	9/22/25	9/27/25
	(28) 10 - 12 - 14 - 16 FAIRWAY DRIVE	0%	9/29/25	10/4/25
	(29) 18 - 20 - 22 - 24 FAIRWAY DRIVE	0%	10/6/25	10/11/25
T	(1) 81 - 82 - 83 - 84 FIVE POND CIRCLE	0%	9/1/25	9/6/25
E	(2) 71 - 72 - 73 - 74 FIVE POND CIRCLE	0%	9/8/25	9/13/25
A	(3) 61 - 62 - 63 - 64 FIVE POND CIRCLE	0%	9/15/25	9/20/25
M	(4) 51 - 52 - 53 - 54 FIVE POND CIRCLE	0%	9/22/25	9/27/25
	(5) 41 - 42 - 43 - 44 FIVE POND CIRCLE	0%	9/29/25	10/4/25
#	(6) 31 - 32 - 33 - 34 FIVE POND CIRCLE	0%	10/6/25	10/11/25
3	(7) 21 - 22 - 23 - 24 FIVE POND CIRCLE	0%	10/13/25	10/18/25
	(8) 11 - 12 - 13 - 14 FIVE POND CIRCLE	0%	10/20/25	10/25/25
	(9) 1 - 2 - 3 - 4 FIVE POND CIRCLE	0%	10/27/25	11/1/25
